

# Raisd Campus — executive progress review

**Purpose:** One pack for senior leadership with current progress charts, milestone intent, and projected goals through Lesotho pilot acceptance and campus expansion.

**Cut:** 5 Oct 2026 · checklist FE snapshot SDD-13 (sheet 19 Sep 2026) · platform readiness includes work since then

**Pilot:** Lesotho (M4) · **SoR this phase:** existing campus CMS family via Portal API (ADR-1)

Live checklist = 0%

FE started ≈ 31%

Platform readiness ≈ 65%

Lesotho pilot decided

Admissions-first sequence

All target weeks TBC

## 1. Executive snapshot

Raisd is building four modern portals (Applicant, Student, Lecturer, Staff) on the **existing campus CMS** through a single Portal API. The Working Group selected **Lesotho as the first acceptance campus (M4)** on 3 Oct 2026. Product sequence remains **admissions-first**: confirm rules (M1) → admissions Live (M2) → core student journeys (M3) → Lesotho acceptance (M4) → other campuses (M5).

**0%**

Checklist Live  
0 of 112 rows Live

**31%**

Frontend started  
32 of 103 applicable

**~65%**

Platform readiness  
Schema · API · docs ·  
inventories

**~20%**

Lesotho pilot (M4)  
Decided · analysed · not  
Live

**How to read the numbers:** Demo / Partial / Placeholder frontend is *started*, not complete. A capability is **Live** only with durable CMS-backed records, server-enforced permissions, and accepted paired staff/lecturer paths. Platform readiness is an engineering estimate — not campus acceptance.

**Leadership tension:** Student UI is deepest (~31% FE started on M3), but product priority is still **M2 admissions on real records**. Do not treat student Demo polish as admissions progress.

## 2. Progress charts

Same figures as the Overview progress board on the docs site ([portal-api-docs/diagrams/#progress](https://portal-api-docs/diagrams/#progress)). Charts below are print-safe (no interactive Mermaid).

### 2.1 Bar — milestone progress %

Frontend started % (sheet) vs estimated platform readiness % (not Live). M1 and M4 have almost no frontend rows.



| MILESTONE                      | FE STARTED  | PLATFORM | WHAT IT MEANS                                                                                                                   |
|--------------------------------|-------------|----------|---------------------------------------------------------------------------------------------------------------------------------|
| M1 Confirm rules & integration | 0%          | ~45%     | Operating / rules milestone. ADR-1, Schema v3 Demo, CAP-53 Partial, architecture docs exist; owners and target weeks still TBC. |
| M2 Admissions launch           | 22% (4/18)  | ~20%     | Student-side starts only. Applicant + staff admissions halves not started. No Live apply→enrol on CMS.                          |
| M3 Core student portal         | 31% (16/51) | ~40%     | Deepest student Demo/Partial. Lecturer and staff paths for the same capabilities still 0.                                       |
| M4 Lesotho pilot acceptance    | 0%          | ~20%     | Pilot decided 3 Oct; screenshot inventory + DB gap probe published. Live SoR path and dump still open.                          |
| M5 Campus expansion            | 35% (12/34) | ~25%     | Sheet starts + campus inventories (Cyberjaya / Botswana / Sierra Leone). Do not pull ahead of admissions Live.                  |

### 2.2 Cumulative readiness over Working Group weeks


Platform work rising; FE started flat at 31% since the 19 Sep sheet; Live stays at 0%. Dates are WG checkpoints, not a committed delivery calendar.

|        |                  |                   |            |
|--------|------------------|-------------------|------------|
| 18 Sep | ~15%<br>Platform | 31%<br>FE started | 0%<br>Live |
| 22 Sep | ~30%<br>Platform | 31%<br>FE started | 0%<br>Live |
| 25 Sep | ~45%<br>Platform | 31%<br>FE started | 0%<br>Live |
| 1 Oct  | ~55%<br>Platform | 31%<br>FE started | 0%<br>Live |
| 3 Oct  | ~60%<br>Platform | 31%<br>FE started | 0%<br>Live |
| 5 Oct  | ~65%<br>Platform | 31%<br>FE started | 0%<br>Live |

| WG DATE     | PLATFORM | FE STARTED | LIVE | WHAT CHANGED                                                            |
|-------------|----------|------------|------|-------------------------------------------------------------------------|
| 18 Sep 2026 | ~15%     | 31%        | 0%   | WG kickoff context; FE snapshot already ~31% from student Demo/Partial. |
| 22 Sep 2026 | ~30%     | 31%        | 0%   | Campus inventories and dump analysis underway.                          |
| 25 Sep 2026 | ~45%     | 31%        | 0%   | Schema v3 Demo and Portal API / CAP-53 Partial strengthen platform.     |
| 1 Oct 2026  | ~55%     | 31%        | 0%   | Docs and campus baselines deepen.                                       |
| 3 Oct 2026  | ~60%     | 31%        | 0%   | Lesotho pilot decided; screenshot inventory and DB gap probe start.     |
| 5 Oct 2026  | ~65%     | 31%        | 0%   | Current cut: platform ~65%; FE sheet still flat; Live still 0%.         |

### 2.3 Pie — work mix (applicable frontend rows)

103 applicable M2+M3+M5 frontend rows. Live = 0 omitted. Totals: started 32 · not started 71 ·  $32 \div 103 \approx 31\%$ .

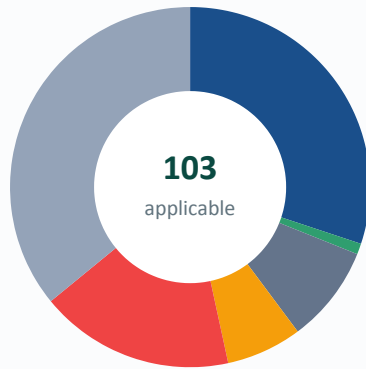


- **Started — Student · 31** — includes 4 M2 student-side starts; not Live
- **Started — Shared (CAP-53) · 1** — Portal API Partial
- **Not started — Student · 9** — of 40 student applicable
- **Not started — Applicant · 7** — entire applicant set (M2 critical path)
- **Not started — Lecturer · 18** — publish / attendance / marking
- **Not started — Admin/staff · 37** — including admissions staff review

**Totals check:** Started  $31 + 1 = 32$  · Not started  $9 + 7 + 18 + 37 = 71$  ·  $32 + 71 = 103$  ·  $\approx 31\%$  FE started (matches KPI and bar chart). Backend remains Needs checking on every applicable row.

### 3. Projection, intentions, and goals

#### 3.1 Intended delivery sequence (order only)

Agreed milestone *order*. Kickoff week and every target week on the sheet remain **TBC**.

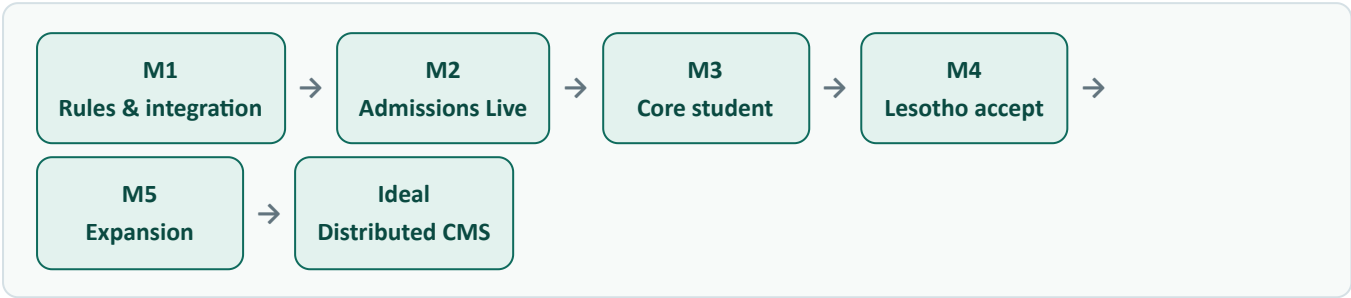

| ORDER | MILESTONE                             | INTENTION                                                                                                        | RELEASE CONDITION (GOAL)                                                     | TARGET        |
|-------|---------------------------------------|------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------|---------------|
| 1     | <b>M1</b> Confirm rules & integration | Name owners, campus rules, API access, operating responsibilities                                                | Rules and integration access agreed — unblocks later Live work               | TBC           |
| 2     | <b>M2</b> Admissions launch           | Applicant apply → evidence → offer → enrol on <b>real CMS records</b> ; Portal API first slice (CAP-53)          | End-to-end admissions Live; staff path via verified old CMS or new screens   | TBC           |
| 3     | <b>M3</b> Core student portal         | Learning, records, fees, registration with lecturer/staff support paths                                          | Student + staff journeys Live with durable records (Demo alone insufficient) | TBC           |
| 4     | <b>M4</b> Lesotho pilot acceptance    | First campus acceptance; parity with Lesotho newer CMS; training & ops                                           | Lesotho campus accepts the integrated pilot                                  | Pilot decided |
| 5     | <b>M5</b> Campus expansion            | Cyberjaya, Eswatini (proposed), Botswana, Sierra Leone, ...; progressive CMS consolidation only on verified gaps | Each campus accepts its rollout; no silent SoR rewrites                      | After M4      |
| Ideal | <b>Distributed Raid CMS</b>           | One product · country/region DBs · white-label · feature flags                                                   | Longer-term target after pilot and expansion evidence                        | Beyond M5     |

#### 3.2 Near-term intentions (next engineering focus)

|                                                                                                                                                                                                                                                                                            |                                                                                                                                                                                                               |
|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <b>Protect admissions-first priority</b> <ul style="list-style-type: none"><li>Freeze non-critical student Demo polish unless it is on the M2 path (auth, accessibility, mobile shell).</li><li>Prioritise CAP-53, applicant CAP-02/03/07/55, and Registry old-CMS verification.</li></ul> | <b>Close leadership blockers (M1)</b> <ul style="list-style-type: none"><li>Named owners for rules, API access, and operating checks.</li><li>Agree kickoff and first target weeks (currently TBC).</li></ul> |
|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|

- Keep student demos labelled Demo until wired to durable SoR.

- Confirm backend commitment path for CMS bridge.

#### Lesotho pilot readiness (M4 path)

- Secure agreed Live SoR path / old CMS dump (no PII in repos).
- Map NMDS, LGCSE, Loti, and newer-CMS parity gaps.
- Treat CAP-41 training/ops as part of acceptance, not an afterthought.

#### Projected outcome for leadership

- **This phase (M1–M4):** modern portals on existing CMS; Lesotho accepts first.
- **Success metric:** Live checklist moves off 0% on admissions, then core journeys.
- **Not the goal yet:** rewriting every staff desk or pulling M5 ahead of M2 Live.

### 3.3 Goals by horizon

| HORIZON              | GOAL                                                          | EVIDENCE OF SUCCESS                                                     | CURRENT STATE (5 OCT)  |
|----------------------|---------------------------------------------------------------|-------------------------------------------------------------------------|------------------------|
| Immediate            | Leadership lock on M1 owners, access, and target weeks        | Named owners + dated plan on the Timeline tab                           | Open / TBC             |
| First Live product   | M2 admissions end-to-end on real records                      | Apply→enrol Live; CAP-53 bridge past stub; staff path verified          | Demo started · Live 0% |
| Core campus journeys | M3 student + lecturer/staff paths Live or verified on old CMS | Durable records; paired role actions accepted                           | Student Demo deepest   |
| Pilot acceptance     | M4 Lesotho campus acceptance                                  | Campus sign-off; parity with newer CMS for accepted journeys; ops ready | Pilot decided · ~20%   |
| Scale                | M5 multi-campus rollout + careful CMS consolidation           | Per-campus acceptance; migration strategy before retiring desks         | Inventories only       |
| Ideal end state      | Distributed Raisd CMS (country DBs, white-label)              | Architecture accepted; no premature rewrite of working SoR              | Documented target      |

### 3.4 Definition of done (any capability)

1. Real data from the system of record (not a mock session).
2. Durable save where the user can mutate data.
3. Server-enforced permission for that role and campus.
4. Paired staff/lecturer action exists in new UI **or** is verified in the old CMS.
5. Accountable owner named.
6. Core mobile accepted if the capability is in the mobile product set.
7. Country/campus operating checks closed or explicitly waived.

## 4. Leadership asks

| # | ASK                                                                                  | WHY IT MATTERS                                               | BLOCKS                    |
|---|--------------------------------------------------------------------------------------|--------------------------------------------------------------|---------------------------|
| 1 | Confirm named owners for campus rules, Portal API access, and operating checks       | M1 release condition; unblocks “Needs checking” backend rows | M2–M4 planning            |
| 2 | Set kickoff and first milestone target weeks (even provisional)                      | Sheet targets are all TBC; sponsors need a calendar signal   | Weekly % credibility      |
| 3 | Commit CMS bridge / Live SoR path for Lesotho (and dump access without PII in repos) | Without this, Live stays at 0% regardless of UI polish       | M2 Live and M4 acceptance |
| 4 | Reaffirm admissions-first priority over further student Demo expansion               | Current build gravity is M3 student UI                       | M2 critical path focus    |
| 5 | Confirm who receives weekly progress PDFs and Demo credentials                       | Governance cadence for senior review                         | Reporting rhythm          |

## 5. Sources and reading notes

| SOURCE                                          | USE IN THIS PACK                                     |
|-------------------------------------------------|------------------------------------------------------|
| SDD-13 Progress timeline (sheet 19 Sep 2026)    | FE started / applicable / Live counts                |
| SDD-03 Delivery milestones (updated 3 Oct 2026) | M1–M5 sequence, Lesotho M4, definition of done       |
| Overview progress board (docs site, 5 Oct 2026) | Charts, platform readiness estimates, WG-week series |
| Working Group 3 Oct 2026                        | Lesotho selected as pilot acceptance campus          |
| ADR-1 (Aslam, 23 Sep 2026)                      | Existing CMS family remains SoR this phase           |
| Weekly pack 2026-10-03                          | Baseline delivery detail for engineering estate      |

Companion weekly engineering pack: docs/reports/weekly-progress-2026-10-03/. Live board: <https://raisd-campus.github.io/portal-api-docs/diagrams/#progress>.
