

Raisd Campus weekly progress

Focus: Full baseline to first weekly cut — Student + Applicant Demo UIs, design system 0.6.1, Portal API + Neon Schema v3 Demo, Vercel PoC estate, LMS docs, LUCT CMS inventories, ADR-1 SoR posture

Window: Working-group formation 18 Sep 2026 → first weekly cut 3 Oct 2026

Cut source: Pulled `raisd-campus/*` mains on 3 Oct 2026 · Prepared by Iman Suherman

First weekly meeting

Live count = 0

ADR-1 confirmed

DS 0.6.1

Schema v3 Demo

Vercel + Neon PoC

Applicant UI started

LMS pages published

CMS hubs CBJ-SL-BW

Owners / dates TBC

1. Executive summary

This is the **first Raisd Campus weekly progress pack**. Because the group has not yet run a recurring weekly cadence, this report covers the **full baseline** from the 18 September working-group meeting through the 3 October cut — not a narrow seven-day delta. Content reflects the campus mains pulled on 3 October 2026 (control-plane f8d54d1, design-system v0.6.1, student/applicant portals, portal-api, docs, db-admin).

The estate is now a working **Demo platform**: four portal webs on Vercel (Student and Applicant with real UI; Lecturer/Staff placeholders), a dedicated **Portal API** service with **Neon Postgres Schema v3** persistence for Demo records, a read-only DB admin, a published shared design system through **0.6.1**, central AI knowledge base + SDD catalogue, LMS architecture/feature pages (Q37 Option 1), and LUCT CMS inventories for Cyberjaya, Sierra Leone, and Botswana.

Product priority remains unchanged: **Cyberjaya first · Admissions before semester registration · core mobile at launch · existing CMS as this-phase system of record** (ADR-1, Aslam 23 Sep 2026). **Live count remains 0**. Demo persistence on Neon is not CMS-acknowledged Live. CAP-53 callable surface, named owners, kickoff, and auth model for campus identity are still open.

0

Capabilities Live
(Demo ≠ done)

0.6.1

Design system
published package

v3

Demo schema
Neon + policy tables

6

Vercel Demo targets
+ Neon + DB admin

727

Student unit tests
(92 files, latest gate)

Started

Applicant Demo UI
(M2 surface)

3

LUCT CMS hubs
CBJ · SL · BW

TBC

Kickoff · owners
CMS Live access

Verdict: Foundations and Demo hosting are strong enough for a weekly operating rhythm and stakeholder walkthroughs. Highest-leverage next moves remain **owners, kickoff, campus auth, file store, and CAP-53 admissions slice** — not more student polish. Applicant Demo UI is now in progress and should stay the frontend centre of gravity for M2.

Status trap. Deployed Vercel URLs and Neon-backed Demo edits are still *Demo*. Live requires real campus data, CMS-acknowledged writes, server-enforced authz, durable evidence store, and an accountable owner. Do not present PoC endpoints as production campus systems.

2. Blockers and decisions needed

Absorbs SDD-10 (including CS-01–CS-13 / Q37 decisions of 1 Oct) and the sequence tension in SDD-03 / SDD-13. Closing D1–D4 unblocks measurable Live progress on M2.

2.1 Blockers

#	BLOCKER	WHAT IS STUCK	STATUS
B1	No named next-action owners	Checklist next-action owners and target weeks remain TBC. Demo work cannot graduate to Live without accountable departments.	Blocked Working group
B2	Kickoff and backend commitment TBC	Timeline tab has no agreed calendar. Milestone targets cannot be planned as dates.	Blocked Working group
B3	CAP-53 callable CMS surface	Dumps inventoried; Portal API Demo uses stub CMS mode. HTTP surface, credentials path, and owning team for Live writes still TBC.	Blocked Q1 / Q2 / Q26
B4	Campus auth model undecided	Demo student-number + password login exists. CMS password vs SSO vs both for applicants/students (Q3) still open for Live.	Blocked Q3
B5	Durable file store undecided	Evidence, assignments, payment proofs need a durable store for Live (Q5). Current portals use session/metadata Demo uploads.	Blocked Q5
B6	Per-campus policy confirmation	Schema v3 Demo seeds university defaults. CS-01–CS-11 must be confirmed per campus before that campus's Live features.	Policy gate Q29–Q35

2.2 Decisions needed this meeting (detail)

These five decisions are the working-group agenda items that unblock Live work on Admissions (M2). Each decision states **why it matters now**, the **options**, the **recommended default** for discussion, and **what happens if we leave it open**. Record the outcome in the checklist Timeline tab and SDD-10 decision log in the same meeting if possible.

D1 — Delivery sequence: keep admissions-first?

Why now. Product priority (7 Sep) is Cyberjaya first and *Admissions before semester registration*. Engineering reality has been the opposite for weeks: Student Demo is deepest (M3 depth). Applicant Demo UI has now started and is deployed — so the sequence question is no longer theoretical. We must either reconfirm M2 as P0 or explicitly change product priority.

OPTION	MEANING	CONSEQUENCE
(a) Reconfirm admissions-first Recommended	Applicant journeys + CAP-53 admissions slice are P0. Student Demo continues only for shared design-system reuse, gate hygiene, and blockers that Applicant also needs.	Build aligns with M2 Live path; student polish is deprioritised.
(b) Promote student Demo as near-term showpiece	Accept that stakeholder walkthroughs centre on enrolled-student UX; Admissions Live slips until CAP-53/Applicant catch up.	Must update the sheet / SDD sequence so the group is not measuring against admissions-first while funding M3 depth.

If we do nothing: effort drifts back to more student Demo while Applicant / Registry Live remains empty. Weekly status will keep looking “busy” without moving Live count off 0 on the critical path.

D2 — CAP-53 / old CMS API ownership and access

Why now. CAP-53 (Portal API ↔ existing Cyberjaya CMS) is the only shared item marked Partial and gates every Live student/applicant write. We have dump inventories and `api_student_*` / desk evidence, but **no named owner**, no granted callable HTTP surface, and Portal API still runs `cms.mode = stub` with Neon Demo persistence. Without D2, Demo forever.

OPTION	MEANING	CONSEQUENCE
(a) Name owner + grant access this week Recommended	Assign a backend / old-CMS owner. Grant read (then controlled write) access for an admissions slice: apply → evidence → offer → enrol mapping to existing SPs/tables.	Engineering can start a real CAP-53 spike with evidence, not guesses.
(b) Time-box a paired spike	Frontend + CMS pair for 3–5 days to document callable methods, auth, and first write path; owner named by end of spike.	Faster discovery if a single owner is not ready, but still needs access credentials.

Related open questions: Q1 (stack/access), Q2 (CMS owner / callable surface), Q26 (map `api_student_*` / `portal_r_student_*` to Portal API methods).

If we do nothing: Neon Demo keeps looking “persistent” while Live count stays 0. Applicant UI cannot graduate beyond Demo.

D3 — Cyberjaya Live login path (CAP-01)

Why now. Student Demo already has student-number + password login (gitignored credentials; Portal API validates). That is *not* campus identity. Applicants and enrolled students need an agreed Live path before CAP-01 can leave Demo/Placeholder. Choice also drives Portal API session design, password reset ownership, and whether applicants share the same IdP as students/staff.

OPTION	MEANING	BEST FIT
(a) CMS credentials via Portal API	Portal API authenticates against existing CMS user store / login rules; issues portal session only after CMS accepts.	Fastest path if CMS login is already the campus source of truth.
(b) Campus SSO with CMS mapping	External IdP (SSO); Portal API maps identity to CMS person/student/staff records before authorising.	Better long-term UX; needs IdP owner + attribute mapping + fallback for applicants who are not yet “users”.
(c) Both, with a clear primary Likely	e.g. applicants use CMS/account-create path; enrolled students/staff use SSO (or the reverse). Document primary per audience.	Matches mixed campus reality; must avoid two conflicting passwords without a policy.

If we do nothing: CAP-01 cannot go Live; every journey that assumes real sign-in stays Demo theatre.

D4 — Named department owners and kickoff week

Why now. All checklist next-action owners and target weeks remain TBC. Schema v3 also needs per-campus policy confirmation (CS-01–CS-11) from Registry / Bursary / IT before Live features. Without names and a kickoff week, weekly meetings have no calendar and “Needs checking” never closes.

SEAT TO NAME	WHAT THEY OWN FOR M1–M2
Registry	Admissions rules, offer/enrolment decisions, academic status policy (CS-01–CS-04), CAP-05/06/07 staff path on old CMS
Faculty	Programme/module rules that affect registration later; training readiness toward M4
Bursary / Finance	Fee items, proof-to-allocation, refund/adjustment policy (CS-08–CS-10), bank instructions (Q19)
QA / AQA	Acceptance criteria language; what “Live” means for campus pilot
Marketing	Announcements / recruitment copy only — does not issue offers (CAP-16)
IT / old CMS	CAP-53 access, environments, backups (CAP-38), LoginActive / RBAC mapping (CS-11)

Also decide: a kickoff week (even if later milestone end dates stay TBC). One calendar anchor is enough to start M1/M2 tracking.

If we do nothing: SDD-13 stays “all TBC”; Demo work has no accountable path to Live; weekly packs cannot report closed decisions.

D5 — Durable file store for Live evidence

Why now. Admissions evidence (CAP-03), profile documents (CAP-09), assignment files (CAP-20), and payment proofs (CAP-46) all require a store staff workflows can open. Current portals keep session/metadata Demo uploads only. Choosing the store early avoids rebuilding Applicant upload UX twice.

OPTION	MEANING	TRADE-OFF
(a) Reuse existing CMS document trees / stdfile paths Recommended default	Portal API writes files through the same channels staff already use in the old CMS.	Least migration risk; constrained by legacy layout and access rules; needs owner confirm of live paths (Q25).
(b) Object store + CMS metadata linkage	New blob store for bytes; CMS (or Portal API) holds metadata and ACL.	Cleaner modern path; more infra + dual-read during transition; still needs CMS visibility for staff desks.
(c) Defer Live files; Demo metadata until M3	Keep Applicant/Student uploads as Demo-only until after core journeys exist.	Unblocks screens faster but blocks M2 Live for any journey that legally needs evidence on file.

If we do nothing: CAP-03 / 09 / 20 / 46 cannot go Live; Admissions launch cannot meet “real records” release conditions.

Meeting ask: Vote or assign D1–D5 before deep feature demos. Minimum useful outcome today: D1 choice recorded, D2 owner named (or spike dated), D4 kickoff week + at least Registry and IT owners named.

2.3 Decisions already recorded

DATE	DECISION	BY
7 Sep 2026	Cyberjaya first; admissions before registration; core mobile; keep existing CMS; five portal groups	Product owner (sheet)
22–23 Sep 2026	Central docs/ai/ SSOT; student docs extracted; ADR-1 SoR + progressive unified CMS	Faid / Aslam / Engineering
28–29 Sep 2026	Demo sign-in (student number + password); Vercel + Neon PoC estate deployed (not Live architecture)	Faid request / Engineering
1 Oct 2026	Canonical Schema v3 with university-default → campus-override policy hierarchy; CS-01–CS-11 are Live readiness, not schema blockers	Architecture + Engineering
1 Oct 2026	Q37 Option 1 — publish Raisd LMS pages from CAP + F01–F37 (no PPA comparison in this set)	Iman / Product architecture

DATE	DECISION	BY
1–2 Oct 2026	Design system releases through 0.6.1; Applicant Demo UI preview; campus repo sync	Engineering

3. Proposed meeting agenda

#	TOPIC	TIME HINT	OUTCOME
01	Demo vs Live language + PoC disclaimer	5 min	Shared status words
02	Executive KPIs and sequence (M2 vs M3)	5 min	Align D1
03	Walkthrough: Student Demo + Applicant Demo (optional)	12 min	UI awareness, not acceptance
04	Portal API / Neon Schema v3 + Vercel estate	8 min	Understand Demo persistence limits
05	LMS pages + CMS hubs + ADR-1 reuse posture	5 min	No accidental rebuild of desks
06	Blockers B1–B6 and decisions D1–D5	15 min	Named owners / votes
07	Next-week plan + Q&A	5 min	Agreed focus

Hard stop suggestion: 55 minutes. If D1–D4 are still open at minute 30, defer deep feature demos.

4. What this pack is (and is not)

WE WILL COVER

- Full baseline from WG start to 3 Oct (first weekly)
- Demo / Partial / Live language from the checklist glossary
- Student + Applicant Demo progress and design system 0.6.1
- Portal API + Neon Schema v3 + Vercel PoC endpoints
- LMS docs (Q37), CMS inventories, ADR-1 SoR
- Explicit decisions required to unblock Live M2


WE WILL NOT CLAIM

- That any capability is Live or campus-accepted
- That Vercel/Neon is production architecture (UltraHost/k3s remains SDD-12)
- That Neon Demo writes are CMS-acknowledged
- That Schema v3 university defaults are signed LUCT policy
- That Botswana / Sierra Leone inventories imply next Live campus
- Native-app delivery (core mobile = phone-friendly web)

THE POINT: Establish a weekly rhythm with honest status. Demo platform is walkable; Live admissions still needs owners, access, auth, files, and CAP-53.

5. Delivery sequence vs build centre of gravity


Milestone order follows the admissions-first decision. Bars below are **order only**; every target week on the sheet remains TBC.

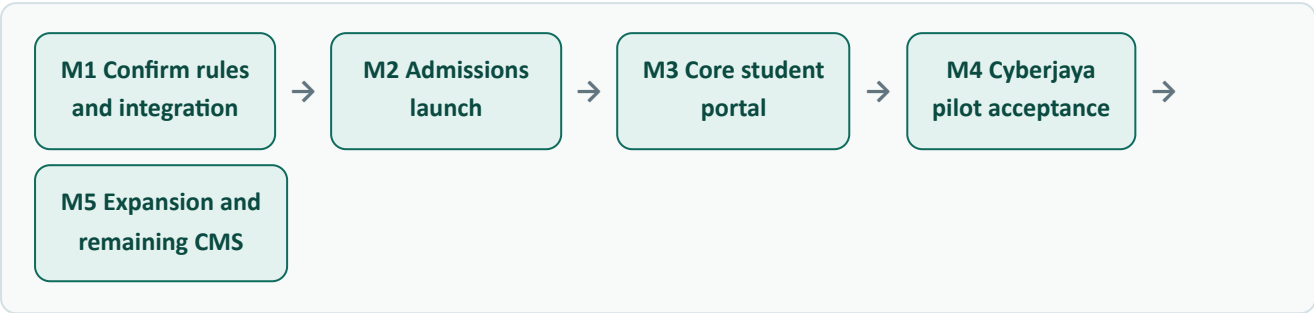

MILESTONE	TARGET	MUST WORK	ENGINEERING NOW (3 OCT)
M1 Confirm rules & integration	TBC	Rules, owners, old-CMS access, operating responsibilities	Schema policy framework + CMS inventories advanced; owners/access still open
M2 Admissions launch	TBC	Apply → evidence → offer → enrol on real records	Applicant Demo UI started · CAP-53 still stub · Staff admissions prefer old CMS
M3 Core student portal	TBC	Learning, timetable, assignments, fees, registration + lecturer/staff paths	Student deep Demo · Neon-backed session state · lecturer/staff paths Not started
M4 Cyberjaya pilot acceptance	TBC	Integrated pilot, training, campus accept	Operating readiness only (CAP-41 Not started)
M5 Expansion & remaining CMS	TBC	Other campuses + progressive consolidation on verified gaps	SL/BW hubs + LMS research published; do not pull ahead of M2 Live

5.1 Frontend started vs not started (sheet snapshot basis)

Filled = frontend started on Faid sheet detailed tab (SDD-13, 19 Sep download; status cells unchanged at last sheet pull). Engineering has since started Applicant Demo UI — sheet rows may lag; Live remains 0 either way.

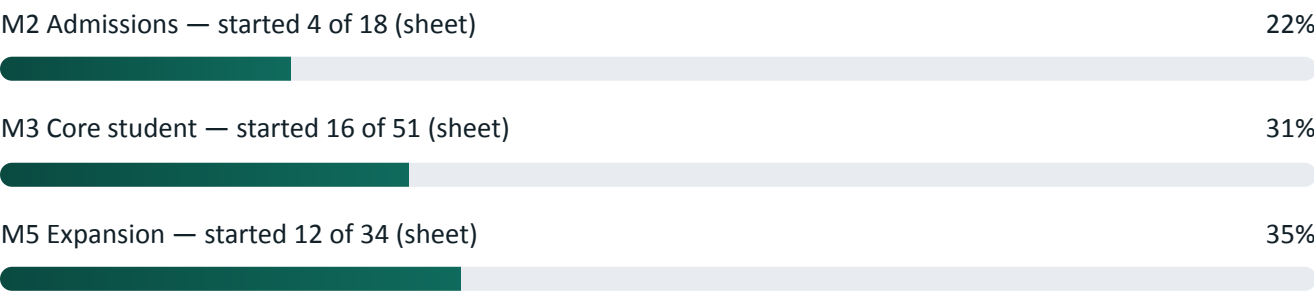

Tension easing, not resolved: Applicant Demo UI finally moves engineering toward M2, but Student Demo remains deepest. Keep Applicant + CAP-53 as P0 until D1 says otherwise.

6. What has been delivered (baseline to 3 Oct)

6.1 Product baseline and knowledge system

- **SDD catalogue** SDD-00–15 with nomenclature anchors; open questions extended for Schema CS-01–CS-13 and LMS Q37.
- **Central AI knowledge base** at `control-plane/docs/ai/` — agents across sibling repos point here as SSOT.
- **Published docs site** — architecture, ERD (Schema v3), LMS hubs, CMS inventories, OpenAPI HTML, PoC page, design-system catalogue, site search.
- **Stack config** `repositories.yaml` + shared portal CI/CD template; git/CI status tooling.

6.2 Student portal (Demo — deepest Raisd UI)

- Cyberjaya enrolled-student journeys: Academic, Profile, Online Forms, Immigration, Finance, Announcements, Policies, Services, Community.
- **Demo sign-in + logout** (Faid, 28–29 Sep): student number + password; credentials from gitignored control-plane file; HTTP login via Portal API.
- Responsive 375–1440px; shared portal shell from design system; Chromium + WebKit gates.
- **Latest recorded gate:** 727 unit tests / 92 files; ~271 Chromium / 35 WebKit with intentional skips; production build + bundle budgets.
- Pins `@raisd-campus/design-system@0.6.1`. Deployed Demo: <https://raisd-student-portal.vercel.app>.

6.3 Applicant portal (Demo — M2 surface now started)

- Applicant UI preview with application checklist, fee/review summaries, Transfer Proof disclosure, reviewer messages (session-only).
- Uses shared design system 0.6.1 (fields, conversation, survey/accordion patterns).
- CI/CD deploys main to <https://raisd-applicant-portal.vercel.app>.
- Still Demo — no Live CMS admissions writes; automated Applicant test suite not yet established as a full gate.

6.4 Design system

- Published through **v0.6.1** (GitHub Packages): portal shell, survey layout, conversation/chat presentation, standard 36px fields, record summary cards, and related patterns.
- Catalogue HTML + captures (~89) validated; public mirror PR path documented for portal-api-docs.
- Change-triggered catalogue / Docs-Impact rules for agents and CI.

6.5 Portal API + Schema v3 Demo

- Dedicated `raisd-campus/portal-api` service (Fastify); OpenAPI expanded in control-plane.
- **Schema v3 Demo:** campus policy collections, university-default seeds, projections + SQL reporting views, audit events, `/v1/meta.schemaVersion`, LMS meta surface.

- Demo records persist in Neon across instances/cold starts; `cms.mode = stub` — no Live CMS writes.
- Demo passwords required on login; CI uses throwaway credentials.

6.6 LMS documentation (Q37 Option 1)

- Published: `lms.html`, `lms-architecture.html`, `lms-features.html` from CAP + F01–F37.
- Agent knowledge: `docs/ai/architecture/lms.md` + `lms-schema.md`.
- Student Materials alone is not an LMS (BASE-44). No PPA LMS comparison in this generate set.

6.7 LUCT / existing CMS inventories

CAMPUS / DUMP	WHAT LANDED	USE IN THIS PHASE
Cyberjaya	Source + DB dump inventoried; CAP matrix (SDD-14); E2E hub; Obsidian FSD knowledge	Primary SoR for M1–M4; reuse staff desks
Sierra Leone	Structure dump + E2E hub on Pages	Expansion pattern — not next Live campus
Botswana	Inventory, ERD/DFD, E2E hub, DTEF / TEF.gov.bw sync	Expansion / scholarship evidence — not next Live campus

7. Demo estate (Vercel + Neon) — not production

PoC path deployed 28–29 September 2026. **Not an ADR.** Production remains UltraHost + k3s; existing CMS stays SoR for Live writes (ADR-1 / SDD-12).

TARGET	URL / LOCATION	STATE
Student portal	https://raisd-student-portal.vercel.app	Demo UI · CI/CD on main
Applicant portal	https://raisd-applicant-portal.vercel.app	Demo UI · CI/CD on main
Lecturer portal	https://raisd-lecturer-portal.vercel.app	Coming soon placeholder
Staff portal	https://raisd-staff-portal.vercel.app	Coming soon placeholder
Portal API	https://raisd-portal-api.vercel.app	Demo API · manual deploy; CI smoke checks
Neon Postgres	neondb · aws-ap-southeast-1	Schema v3 Demo records
DB admin	https://raisd-db-admin.vercel.app (team)	Read-only browser
Public docs	https://raisd-campus.github.io/portal-api-docs/	OpenAPI · diagrams · PoC page

PoC limits: no CMS; free-tier Neon cold starts; shared Demo students; session rows accumulate; credentials stay in gitignored control-plane/.credentials/. Never present these URLs as Live campus systems.

8. Capability status snapshot


Sheet columns from SDD-13 (19 Sep). Engineering notes reflect 3 Oct cut where they diverge. Live = 0 everywhere.

PORTAL / SURFACE	SHEET STARTED	LIVE	ENGINEERING READ (3 OCT)
Applicant	0 of 7	0	Demo UI started — update sheet
Student	31 of 40	0	Deep Demo + Neon
Lecturer	0 of 18	0	Placeholder deploy only
Admin / staff	0 of 37	0	Prefer old CMS desks
Shared system	CAP-53 Partial	0	Portal API Demo / stub CMS

8.1 M2 critical path

ID	SURFACE	TASK	NOW
CAP-02 / 03 / 07 / 55	Applicant	Apply, evidence, track/offer/accept, declarations	Demo UI in progress — not Live
CAP-01	Applicant / Student	Sign-in and account	Student Demo password login · Applicant Demo · campus identity TBC
CAP-03/05/06/07	Staff	Review evidence, quals, offer, first enrolment	Not started as Raisd app — use old CMS unless gap
CAP-53	Shared	Portal API ↔ existing CMS	Partial / stub — gates Live
CAP-35 / 36	Applicant	Accessible forms · mobile shell	Responsive work in progress via shared DS — not Live acceptance

9. Architecture and SoR posture

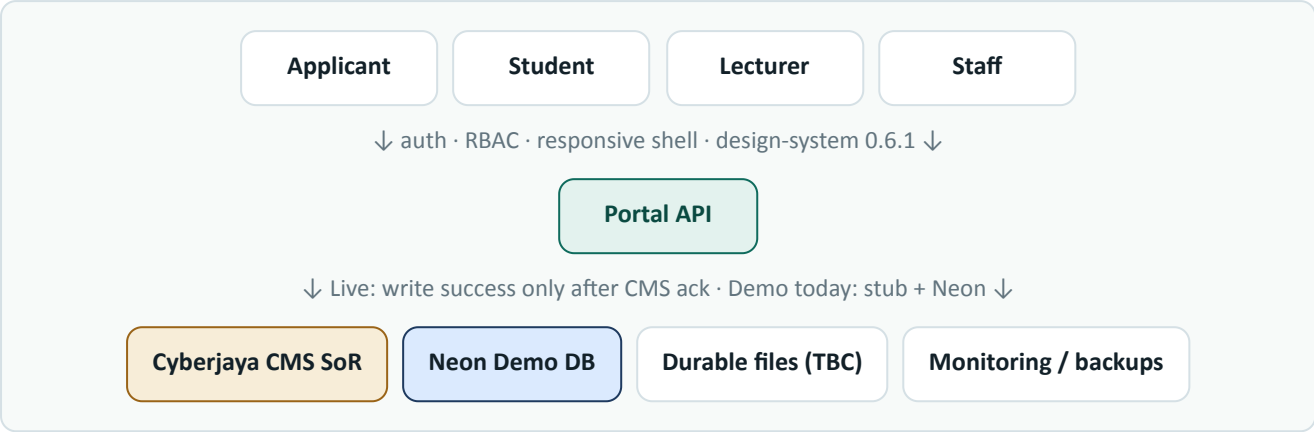

HORIZON	WHAT WE DELIVER	SYSTEM OF RECORD
This phase (M1–M4)	Modern portal UX via Portal API; staff ops on verified old desks unless gap proven	Existing Cyberjaya CMS
Demo PoC (now)	Walkable portals + API + Schema v3 on Vercel/Neon	Neon Demo only — not campus SoR
Longer term (M5+)	Campus expansion + progressive consolidation toward one-stop CMS	Migrate domain-by-domain after verified gap + migration strategy

Schema v3 hierarchy: canonical vocabulary → university default → campus override (effective-dated). Incomplete campus policy confirmation blocks that campus’s Live feature only — not the schema. Demo defaults are structural examples until department sign-off.

10. Repository estate and verification

REPOSITORY	OWNS	BASELINE STATE (3 OCT PULL)
control-plane	SSOT docs, SDD, OpenAPI, stack tooling	Active SSOT · f8d54d1
student-portal	Enrolled-student web	Deep Demo · DS 0.6.1 · Vercel
applicant-portal	Online registration	Demo UI started · Vercel
portal-api	Only HTTP surface portals call	Neon Schema v3 · stub CMS
design-system	Shared tokens/components	v0.6.1 published
portal-api-docs	Public OpenAPI + diagram mirrors	Publishing
db-admin	Read-only Neon browser	Deployed (team)
lecturer-portal / staff-portal	Role webs	Placeholder + CI/CD

10.1 Quality gates (latest recorded)

- **Student:** lint, 727 unit tests / 92 files, production build/isolation, bundle budgets, Chromium/WebKit matrices (some known date-dependent fixture failures on full runs; focused retries green).
- **Design system:** typecheck, unit + consumer fixture + browser checks per release; package published via CI.
- **Portal API:** CI smoke (health, meta, login, wrong password 401, portal call, logout revoke).
- **Applicant:** TypeScript/build + manual responsive review; automated suite still thin vs Student.
- Physical iPhone confirmation remains the final device check for some shell behaviours.

11. Proposed next week and asks

PRIORITY	WORK	WHY
P0	Close D1–D4 in this meeting; write owners into the checklist Timeline tab	Unblocks calendar and accountability
P0	CAP-53 admissions slice spike: map callable CMS surface → Portal API methods	Only path from Neon Demo to Live writes
P1	Continue Applicant Demo toward CAP-02/03/07 completeness; add Applicant automated smoke	Aligns build with M2
P1	Auth decision write-up (CMS vs SSO) with Cyberjaya constraints	Closes B4 / Q3
P2	Refresh Faid sheet Applicant rows to Demo where engineering has started	Stops false “0 of 7” narrative
P2	Keep student work limited to shared DS reuse / gate hygiene unless D1 changes	Protects sequence

11.1 Asks of the working group

- Name owners for Registry, Faculty, Bursary, QA, Marketing, IT, and old-CMS API access.
- Reconfirm admissions-first now that Applicant Demo exists (D1).
- Pick a kickoff week even if later milestones stay TBC.
- Grant (or schedule) access to callable CMS APIs/environments for CAP-53.
- Agree file-store posture for evidence (D5).
- Confirm who should receive weekly PDFs / Vercel Demo credentials.

12. Sources and status language

SOURCE	ROLE IN THIS PACK
Faid Daily Checklist / SDD-13	Sheet FE start counts; Live = 0
SDD-00...15 / docs/ai/	Architecture, milestones, CAP catalogue, open questions
Student + Applicant handoff / README	Verification and Demo depth
vercel-neon-poc.md	Demo estate endpoints and limits
Canonical schema LUCT readiness	Schema v3 + CS-01–CS-13
Aslam WG chat 23 Sep 2026	ADR-1 SoR confirmation
Pulled raisd-campus/* mains 3 Oct 2026	Engineering cut for this PDF

12.1 Status glossary

TERM	MEANING
Demo	UI/API on sample or temporary/Neon Demo data; no Live CMS ack; no campus acceptance
Placeholder	Screen or control exists; intended action does not
Partial	Some of the capability exists; key workflow or acceptance missing
Live	Accepted, real data, access controls, accountable owner
Needs checking	Not verified with owning department or old-CMS owner
PoC	Vercel/Neon demonstration path — not production architecture

Pack path: docs/reports/weekly-progress-2026-10-03/. Subsequent weeks should keep this layout and lead with a week-over-week delta.
