

Raisd Campus — executive progress summary

Purpose: Concise overall project progress report for senior leadership — percentages, milestone readiness, and the path to Live campus acceptance.

Cut: 7 Oct 2026 · FE Demo depth reflects Applicant Demo + hosted Portal API wiring · Live remains checklist-gated

Pilot: Lesotho (M4) · **SoR this phase:** existing campus CMS family via Portal API (ADR-1)

Live checklist = 0%

FE Demo depth ≈ 36%

Platform readiness ≈ 72%

Applicant Demo HTTP live

Schema v4 Demo

Admissions-first sequence

1. Executive snapshot

Raisd is delivering four modern portals — Applicant, Student, Lecturer and Staff — on the **existing campus CMS** through one Portal API. The Working Group selected **Lesotho as the first acceptance campus (M4)** on 3 Oct 2026. Product sequence remains **admissions-first**: confirm rules (M1) → admissions Live (M2) → core student journeys (M3) → Lesotho acceptance (M4) → other campuses (M5).

Since the 5 Oct pack, the Demo estate has taken a material step on the admissions path: the hosted Portal API now runs **Student schema v4** and exposes **Applicant Demo HTTP**, with the Applicant portal wired to that API in production Demo hosting. That improves platform readiness and admissions Demo depth. It does **not** move Live %.

0%

Checklist Live
0 of 112 rows Live

~36%

Frontend Demo depth
37 of 103 applicable ·
eng. cut

~72%

Platform readiness
Schema v4 · API · docs
· Demo host

~22%

Lesotho pilot (M4)
Decided · analysed ·
not Live

How to read the numbers: **Live** is the only completion word on the Working Group checklist — durable CMS-backed records, server-enforced permissions, and accepted paired staff/lecturer paths. **Frontend Demo depth** counts Demo / Partial / Placeholder journeys in the current estate (sheet baseline plus Applicant Demo since 19 Sep). **Platform readiness** is an engineering estimate of integration readiness — not campus acceptance.

Leadership message: Foundations and Demo hosting are now strong enough to support an admissions operating rhythm. The binding constraint remains **M2 Live on real CMS records** — not further student polish. Applicant Demo HTTP proves the portal shape; it does not replace Registry, CMS bridge, or Live auth.


MEASURE	5 OCT	7 OCT	EXECUTIVE READ
Checklist Live	0%	0%	Unchanged — Demo persistence is not Live.
Frontend Demo depth	~31% (sheet only)	~36%	+5 Applicant Demo capabilities counted; WG sheet export still 19 Sep.
Platform readiness	~65%	~72%	Schema v4 reseed, Applicant HTTP, CORS/applicant SPA, OpenAPI 0.4.2.
M2 Admissions FE / platform	22% / ~20%	~50% / ~40%	Largest relative gain this cut — still Demo, not Live apply→enrol.
Lesotho pilot (M4)	~20%	~22%	Slight platform lift only; Live SoR path and dump access still open.

2. Progress charts

Print-safe charts aligned to the Overview progress board ([portal-api-docs/diagrams/#progress](#)), cut 7 Oct 2026.

2.1 Bar — milestone progress %

Frontend Demo depth % vs estimated platform readiness % (not Live). M1 and M4 have almost no frontend rows.

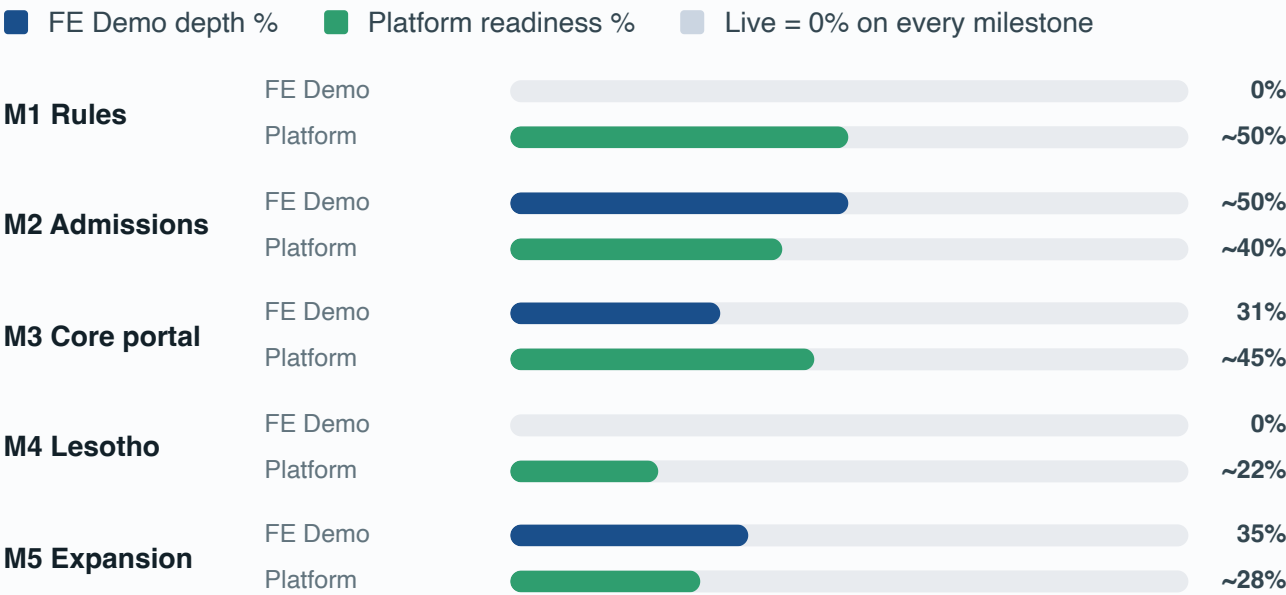

MILESTONE	FE DEMO	PLATFORM	WHAT IT MEANS FOR LEADERSHIP
M1 Confirm rules & integration	0%	~50%	ADR-1, Schema v4 Demo, CAP-53 Partial, and architecture docs exist. Named owners, kickoff, and backend commitment remain TBC.
M2 Admissions launch	~50% (9/18)	~40%	Applicant Demo UI + hosted HTTP now started alongside earlier student-side placeholders. Staff admissions review and Live CMS apply→enrol remain open.
M3 Core student portal	31% (16/51)	~45%	Deepest student Demo. Lecturer and staff paths for the same capabilities remain 0. Schema v4 strengthens the academic/profile model only.
M4 Lesotho pilot acceptance	0%	~22%	Pilot decided; analysis published. Live SoR path, dump access, and NMDS/LGCSE/Loti parity still block acceptance.
M5 Campus expansion	35% (12/34)	~28%	Inventories and dumps analysed for later rollout. Do not pull ahead of admissions Live.

2.2 Cumulative readiness over Working Group weeks


Platform work continues to rise. FE Demo depth moves on 7 Oct with Applicant Demo counted. Live stays at 0%. Dates are WG checkpoints, not a committed delivery calendar.

18 Sep	~15% Platform	31% FE	0% Live
25 Sep	~45% Platform	31% FE	0% Live
3 Oct	~60% Platform	31% FE	0% Live
5 Oct	~65% Platform	31% FE	0% Live
7 Oct	~72% Platform	~36% FE	0% Live

WG DATE	PLATFORM	FE DEMO	LIVE	WHAT CHANGED
18 Sep 2026	~15%	31%	0%	WG kickoff; student Demo/Partial already on the sheet.
25 Sep 2026	~45%	31%	0%	Schema v3 Demo and Portal API / CAP-53 Partial.
3 Oct 2026	~60%	31%	0%	Lesotho pilot decided; inventories begin.
5 Oct 2026	~65%	31%	0%	Prior executive cut; FE still sheet-flat.
7 Oct 2026	~72%	~36%	0%	Current cut: Schema v4 + Applicant Demo HTTP hosted; FE Demo depth lifts on admissions.

2.3 Pie — work mix (applicable frontend rows)

103 applicable M2+M3+M5 frontend rows. Live = 0 omitted. Engineering cut 7 Oct: started **37** · not started **66** · $37 \div 103 \approx 36\%$.

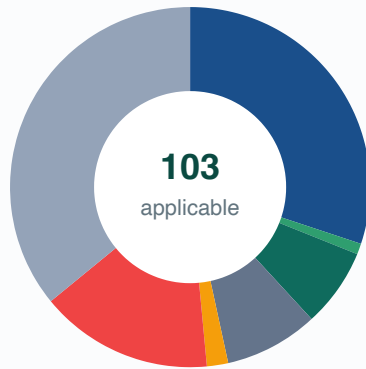

- **Started — Student · 31** — deepest Demo; includes 4 M2 student-side starts
- **Started — Shared (CAP-53) · 1** — Portal API Partial
- **Started — Applicant · 5** — Demo UI + hosted HTTP (sign-in, apply, evidence, track/accept, declarations)
- **Not started — Student · 9**
- **Not started — Applicant · 2** — e.g. announcements / residual mobile shell depth
- **Not started — Lecturer · 18**
- **Not started — Admin/staff · 37** — includes admissions staff review

Totals check: Started $31 + 1 + 5 = 37$ · Not started $9 + 2 + 18 + 37 = 66$ · $37 + 66 = 103$ · $\approx 36\%$ FE Demo depth. Backend remains Needs checking on every applicable checklist row until Live CMS access is confirmed.

3. What moved since 5 October

Hosted Portal API

Student Demo schema now **v4**
after Neon backup and controlled reseed. Applicant Demo RPC is live
(`/v1/auth/applicant/login`, `/v1/applicant/:method`).

Applicant portal

Production Demo build calls the Portal API when configured. Local development can still use the in-process mock. Development Admin Actions stay mock-only.

Public documentation


OpenAPI **0.4.2**
, PoC page, SDD increments, and AI knowledge published on GitHub Pages.

Still not Live: CMS-acknowledged writes, durable evidence bytes, production applicant identity, Registry/staff admissions desks, and Lesotho government-parity acceptance.

4. Projection, intentions, and goals

4.1 Intended delivery sequence (order only)

Agreed milestone *order*. Kickoff week and every target week on the sheet remain **TBC**.

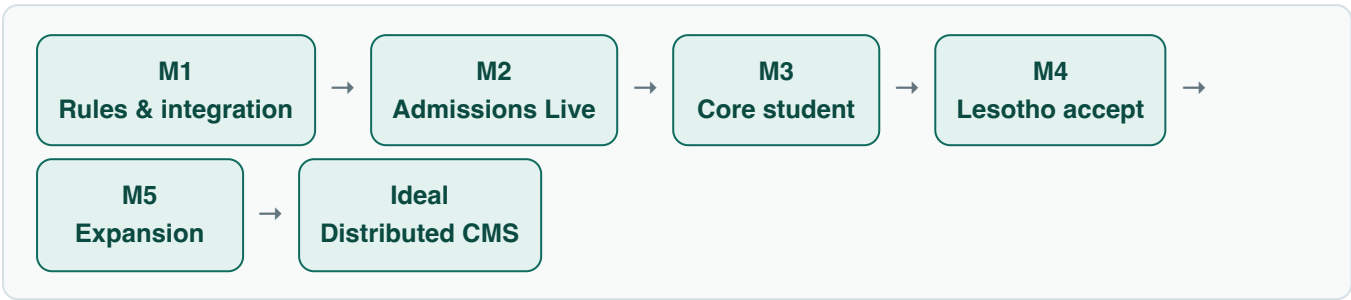

4.2 Near-term intentions

Convert Applicant Demo into M2 Live path

- Bridge CAP-53 from stub CMS to agreed Live SoR path.
- Close applicant identity / auth for Live (Q3).
- Verify Registry / Finance review path on old CMS or new staff screens.

Close leadership blockers (M1)

- Named owners for rules, API access, and operating checks.
- Agree kickoff and first target weeks (currently TBC).
- Confirm backend commitment for the CMS bridge.

Lesotho pilot readiness (M4 path)

- Secure Live SoR path / dump access (no PII in repos).
- Map NMDS, LGCSE, Loti, and newer-CMS parity gaps.
- Treat CAP-41 training/ops as part of acceptance.

Projected outcome for leadership

- This phase (M1–M4):** modern portals on existing CMS; Lesotho accepts first.
- Success metric:** Live checklist moves off 0% on admissions, then core journeys.
- Not the goal yet:** rewriting every staff desk or pulling M5 ahead of M2 Live.

4.3 Goals by horizon

HORIZON	GOAL	EVIDENCE OF SUCCESS	CURRENT STATE (7 OCT)
Immediate	Leadership lock on M1 owners, access, and target weeks	Named owners + dated plan on the Timeline tab	Open / TBC
First Live product	M2 admissions end-to-end on real records	Apply→enrol Live; CAP-53 past stub; staff path verified	Applicant Demo HTTP · Live 0%

HORIZON	GOAL	EVIDENCE OF SUCCESS	CURRENT STATE (7 OCT)
Core campus journeys	M3 student + lecturer/staff paths Live or verified on old CMS	Durable records; paired role actions accepted	Student Demo deepest · schema v4
Pilot acceptance	M4 Lesotho campus acceptance	Campus sign-off; parity for accepted journeys; ops ready	Pilot decided · ~22%
Scale	M5 multi-campus rollout + careful CMS consolidation	Per-campus acceptance; migration strategy before retiring desks	Inventories only

4.4 Definition of done (any capability)

1. Real data from the system of record (not a mock session).
2. Durable save where the user can mutate data.
3. Server-enforced permission for that role and campus.
4. Paired staff/lecturer action exists in new UI **or** is verified in the old CMS.
5. Accountable owner named.
6. Core mobile accepted if the capability is in the mobile product set.
7. Country/campus operating checks closed or explicitly waived.

5. Leadership asks

#	ASK	WHY IT MATTERS	BLOCKS
1	Confirm named owners for campus rules, Portal API access, and operating checks	M1 release condition; moves backend off “Needs checking”	M2–M4 planning
2	Set kickoff and first milestone target weeks (even provisional)	Sheet targets are all TBC; sponsors need a calendar signal	Weekly % credibility
3	Commit CMS bridge / Live SoR path for Lesotho (and dump access without PII in repos)	Without this, Live stays at 0% despite Demo HTTP	M2 Live and M4 acceptance
4	Reaffirm admissions-first priority now that Applicant Demo is hosted	Protect focus on CAP-53 + Registry path over non-critical student polish	M2 critical path focus
5	Refresh the Working Group checklist export to recognise Applicant Demo starts	Keeps FE % reporting aligned with the estate sponsors see in Demo URLs	Sheet / executive number consistency

6. Sources and reading notes

SOURCE	USE IN THIS PACK
SDD-13 Progress timeline (sheet 19 Sep 2026)	Baseline FE / applicable / Live counts
SDD-03 Delivery milestones · SDD-04 Applicant increments (7 Oct)	Sequence, admissions Demo HTTP narrative
Overview progress board (docs site, 7 Oct 2026)	Charts and platform readiness estimates
Portal API / Neon Demo (7 Oct 2026)	Schema v4 reseed; Applicant HTTP; CORS applicant origin
Working Group 3 Oct 2026	Lesotho selected as pilot acceptance campus
ADR-1 (Aslam, 23 Sep 2026)	Existing CMS family remains SoR this phase
Prior executive pack 2026-10-05	Comparison baseline for this cut

Live board: <https://raisd-campus.github.io/portal-api-docs/diagrams/#progress>.
Demo Applicant: <https://applicant-portal-lemon.vercel.app> · API meta: <https://raisd-portal-api.vercel.app/v1/meta>.

Raisd Campus · Executive progress summary · 7 October 2026 · Prepared for senior leadership · Pack path: docs/reports/executive-progress-review-2026-10-07/
